


H1 FORWARD TRACKER UPGRADE SCHEDULE

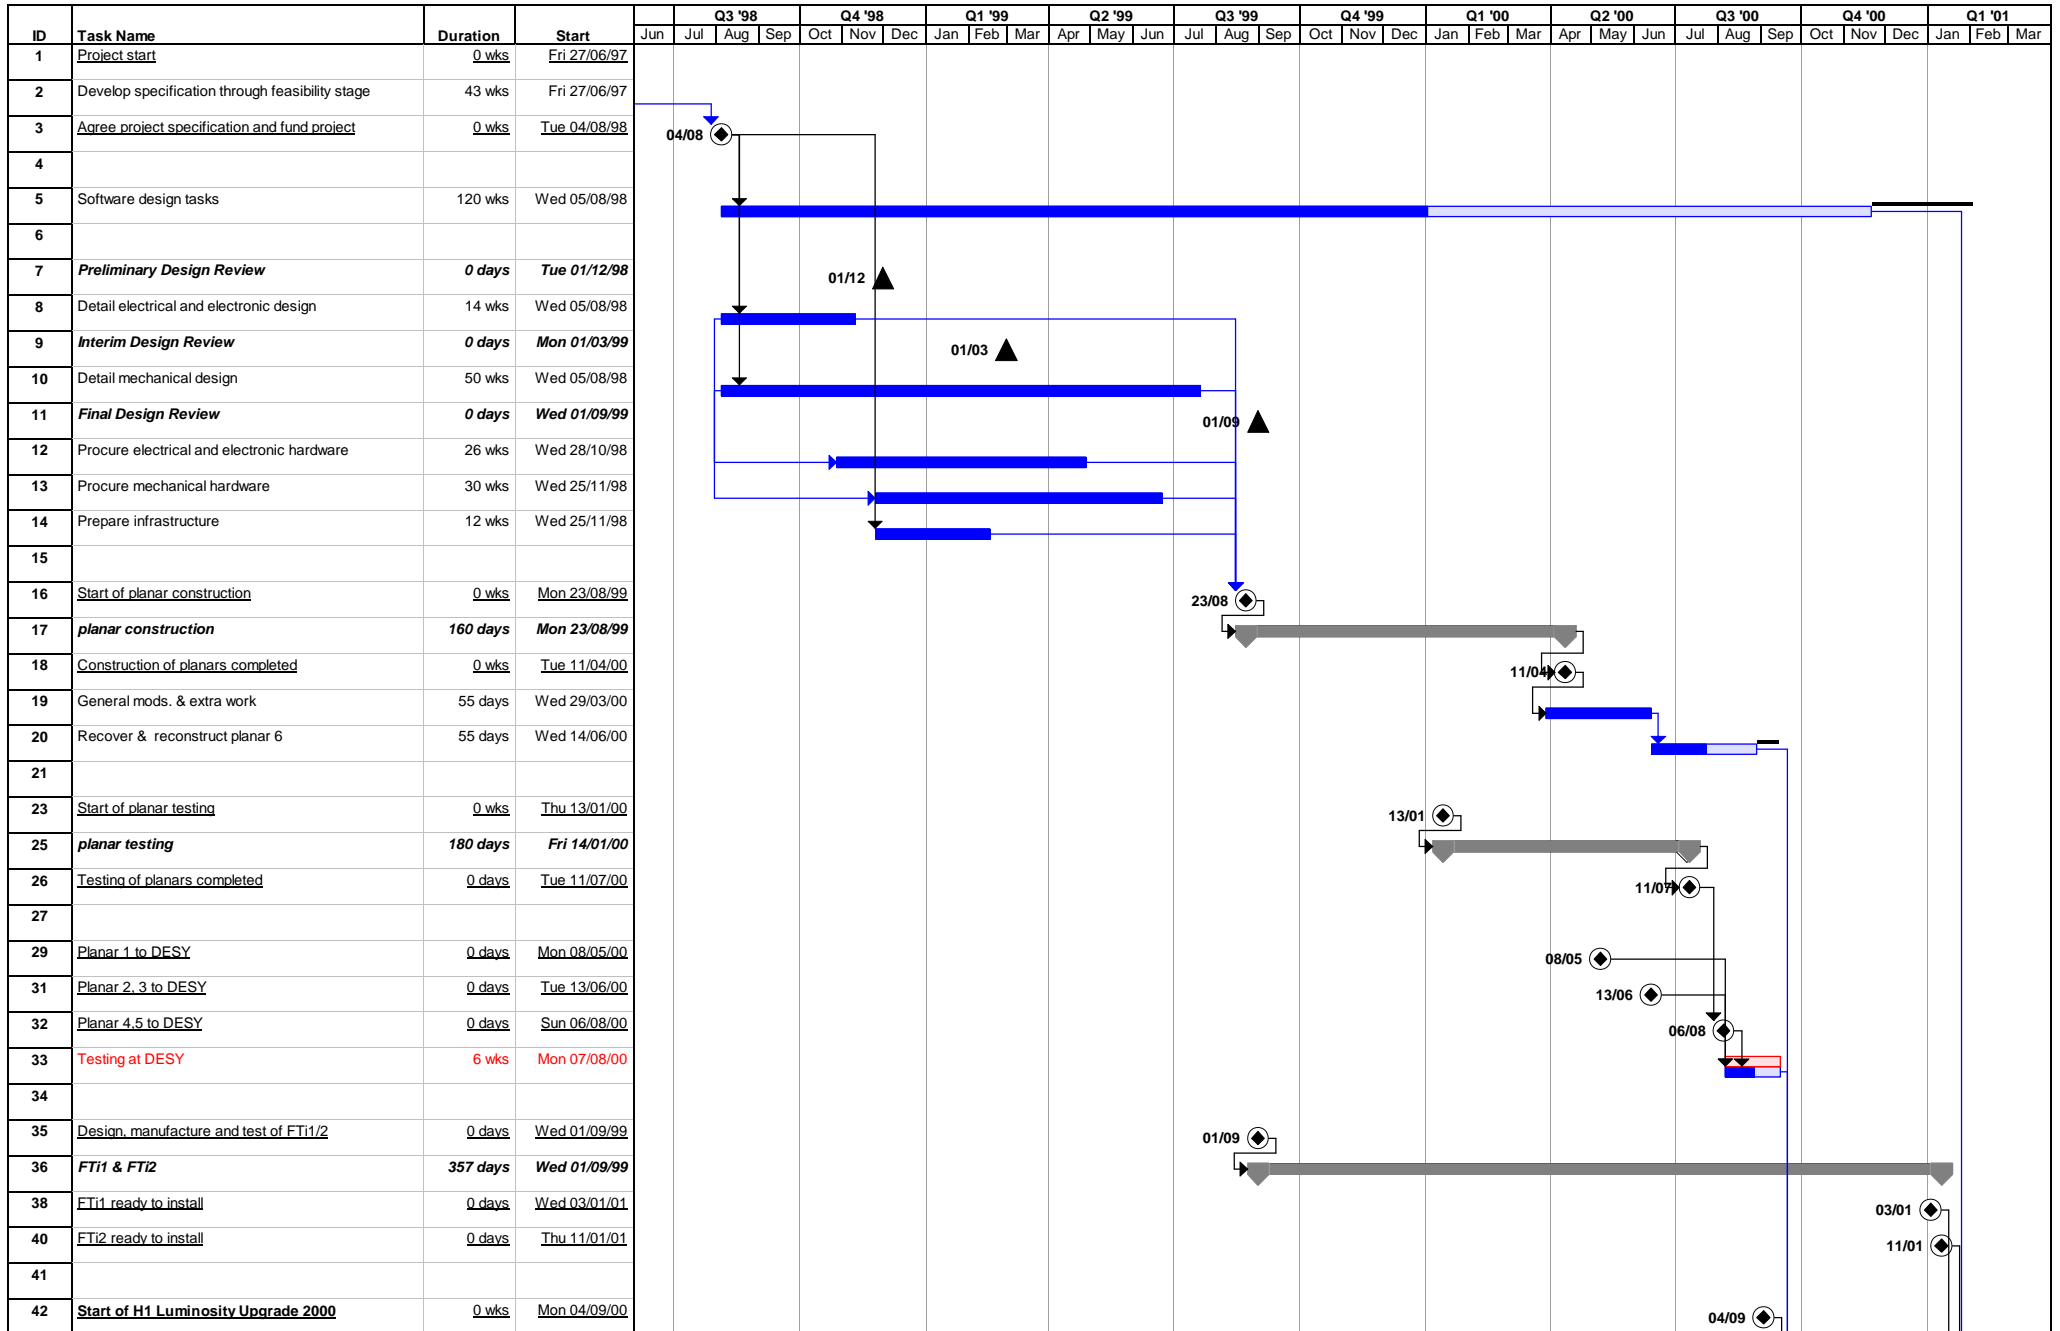

H1 FORWARD TRACKER UPGRADE SCHEDULE

119.513002(version 2.0)
G. Houghton Thu 07/09/00

ID	Task Name	Duration	Start	Q3 '98			Q4 '98			Q1 '99			Q2 '99			Q3 '99			Q4 '99			Q1 '00			Q2 '00			Q3 '00			Q4 '00			Q1 '01														
				Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar											
43	Start removal of FTD	0 days	Mon 04/09/00																								04/09																					
44	FTD removal	3 days	Tue 26/09/00																									28/09																				
45	Removal of FTD complete	0 days	Thu 28/09/00																									29/09																				
46																																																
47	Start of FTD modification	0 days	Fri 29/09/00																																													
48	FTD modification	77.5 days	Fri 29/09/00																																													
49	FTD modifications completed	0 wks	Fri 15/12/00																																													
50																																																
51	Survey FTD	2 days	Mon 18/12/00																																													
52	Start installation of FTi1/FTi2/G0B Support	0 days	Tue 19/12/00																																													
53	Installation of FTi1	3 days	Thu 04/01/01																																													
54	Installation of FTi2	3 days	Fri 12/01/01																																													
55	Installation of FTi1/FTi2/G0B complete	0 days	Tue 16/01/01																																													
56																																																
57	Start installation of FTD	0 days	Tue 30/01/01																																													
58	FTD installation	4 days	Tue 30/01/01																																													
59	FTD installation completed	0 wks	Fri 02/02/01																																													
60	Concluding Review	0 days	Thu 01/03/01																																													

