


H1 FORWARD TRACKER SHUTDOWN SCHEDULE

Thu 11/05/00

| ID | Task Name | Oct | | | | | Nov | | | | | Dec | | | | | |
|----|--|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|-------|
| | | 25/09 | 02/10 | 09/10 | 16/10 | 23/10 | 30/10 | 06/11 | 13/11 | 20/11 | 27/11 | 04/12 | 11/12 | 18/12 | 25/12 | 01/01 | 08/01 |
| 31 | Connect planar 1 feedthroughs, HV test in air | | | | | | | | | | | | | | | | |
| 32 | Bolt planar 0 to U channel & inner tank, & level | | | | | | | | | | | | | | | | |
| 33 | Connect planar 0 feedthroughs, HV test in air | | | | | | | | | | | | | | | | |
| 34 | Replace planar end plate, turn onto radial side, remove radial end plate | | | | | | | | | | | | | | | | |
| 35 | Attach adapter ring to inner tank, bolt planar 4 to U channel/adapter ring & level | | | | | | | | | | | | | | | | |
| 36 | Connect planar 4 feedthroughs, HV test in air | | | | | | | | | | | | | | | | |
| 37 | Box up, HV test all feedthroughs, leak test | | | | | | | | | | | | | | | | |
| 38 | Supermodule 00 complete | | | | | | | | | | | | | | | | |
| 39 | Supermodule 01 (sm01) | | | | | | | | | | | | | | | | |
| 40 | Remove radial end plate | | | | | | | | | | | | | | | | |
| 41 | Remove radial feedthroughs & disconnect signal & HT | | | | | | | | | | | | | | | | |
| 42 | Remove inner/outer bolts, lift radial clear, bag up and store | | | | | | | | | | | | | | | | |
| 43 | Extract transition radiator, bag up & store | | | | | | | | | | | | | | | | |
| 44 | Replace radial end plate, flip & remove planar end plate | | | | | | | | | | | | | | | | |
| 45 | Remove planar 0 feedthroughs & disconnect signal/HT | | | | | | | | | | | | | | | | |
| 46 | Remove inner/outer bolts, lift planar 0 clear, bag up and store | | | | | | | | | | | | | | | | |
| 47 | Remove planar 1 feedthroughs & disconnect signal/HT | | | | | | | | | | | | | | | | |
| 48 | Remove inner/outer bolts, lift planar 1 clear, bag up and store | | | | | | | | | | | | | | | | |
| 49 | Remove planar 2 feedthroughs & disconnect signal/HT | | | | | | | | | | | | | | | | |
| 50 | Remove inner/outer bolts, lift planar 2 clear, bag up and store | | | | | | | | | | | | | | | | |
| 51 | Remove MWPC feedthroughs & disconnect signal/HT | | | | | | | | | | | | | | | | |
| 52 | Remove inner/outer bolts, lift MWPC clear, bag up and store | | | | | | | | | | | | | | | | |
| 53 | Remove inner tank section, modify & replace | | | | | | | | | | | | | | | | |
| 54 | Bolt planar 3 to U channel & inner tank, & level | | | | | | | | | | | | | | | | |
| 55 | Connect planar 3 feedthroughs, HV test in air | | | | | | | | | | | | | | | | |
| 56 | Bolt planar 2 to U channel & inner tank, & level | | | | | | | | | | | | | | | | |
| 57 | Connect planar 2 feedthroughs, HV test in air | | | | | | | | | | | | | | | | |
| 58 | Bolt planar 1 to U channel & inner tank, & level | | | | | | | | | | | | | | | | |
| 59 | Connect planar 1 feedthroughs, HV test in air | | | | | | | | | | | | | | | | |
| 60 | Bolt planar 0 to U channel & inner tank, & level | | | | | | | | | | | | | | | | |

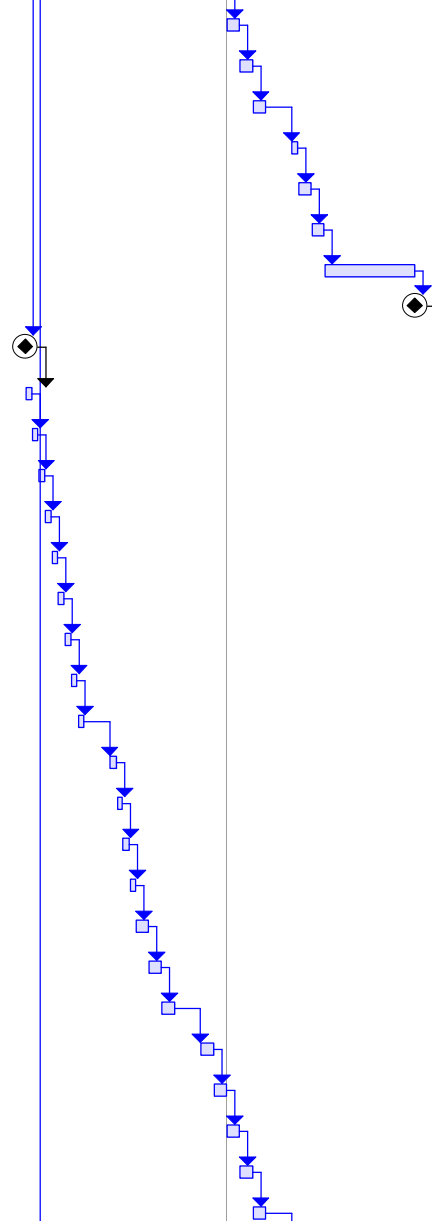

H1 FORWARD TRACKER SHUTDOWN SCHEDULE

Thu 11/05/00

