PLANAR CONSTRUCTION

Fri 24/09/99
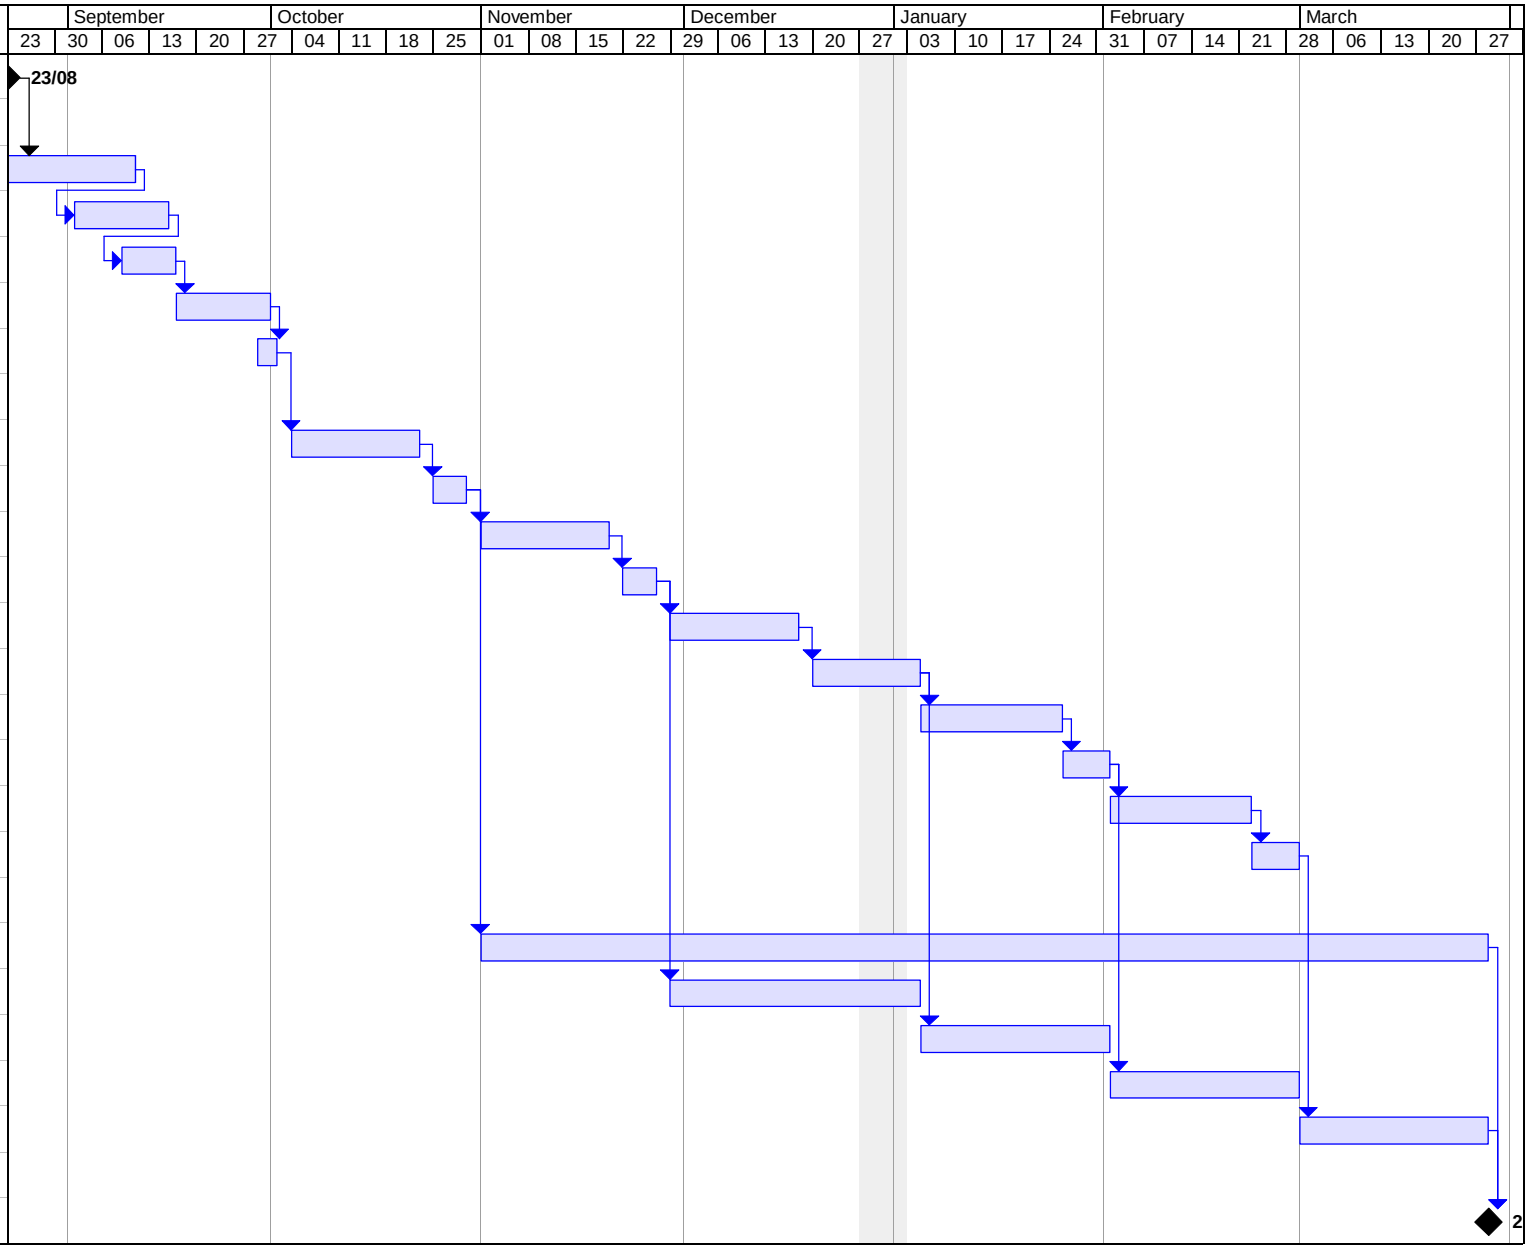
ID	Task Name	Duration
1	**Start planar construction**	**0 days**
2		
3	Clean and HV test PCB's	15 days
4	Bond PCB's to Nomex panels	10 days
5	HV test bonded PCB's	6 days
6	Construct 5 chambers	10 days
7	HV test constructed chambers	3 days
8		
9	Wire and tension test planar no. 1	15 days
10	Contingency for cell failures	5 days
11	Wire and tension test planar no. 2	15 days
12	Contingency for cell failures	5 days
13	Wire and tension test planar no. 3	15 days
14	Contingency for cell failures	5 days
15	Wire and tension test planar no. 4	15 days
16	Contingency for cell failures	5 days
17	Wire and tension test planar no. 5	15 days
18	Contingency for cell failures	5 days
19		
20	Planar no. 1 testing	100 days
21	Planar no. 2 testing	20 days
22	Planar no. 3 testing	20 days
23	Planar no. 4 testing	20 days
24	Planar no. 5 testing	20 days
25		
26	**Planar construction complete**	**0 days**
