H1 FORWARD TRACKER
SHUTDOWN SCHEDULE

Fri 11/12/98

ID	Task Name	Duration
1	FTD available	0d
2	Remove FTD and uncable	7d
3	Move to clean room	1d
4	Split into 3 supermodules	5d
5	Supermodule1	1d
6	Remove radial chamber and tank seg	2d
7	Repair radial module	1d
8	Flip supermodule	0.5d
9	Remove planars	1d
10	Remove MWPCs	1d
11	Planars available	0w
12	Fit 6 wire planar and level	1d
13	Wire-up,solder, plug & test	1d
14	Fit 4 wire planar and level	1d
15	Wire-up,solder, plug & test	1d
16	Fit 4 wire planar and level	1d
17	Wire-up,solder, plug & test	1d
18	Fit 4 wire planar and level	1d
19	Wire-up, solder, plug & test	1d
20	Box up,gas up,volts on and test	3d
21	Flip supermodule	0.5d
22	Install radial chamber and tank segm	2d
23	Reconnect radial chamber	1d
24	Box up,gas up,volts on and test	3d
25	Supermodule2	1d
26	Remove radial chamber and tank seg	2d
27	Repair radial module	1d
28	Flip supermodule	0.5d
29	Remove planars	1d
30	Remove MWPCs	1d
31	Planars available	0w
32	Fit 6 wire planar and level	1d
33	Wire-up, solder, plug & test	1d
34	Fit 4 wire planar and level	1d
35	Wire-up, solder, plug & test	1d
36	Fit 4 wire planar and level	1d
37	Wire-up, solder, plug & test	1d

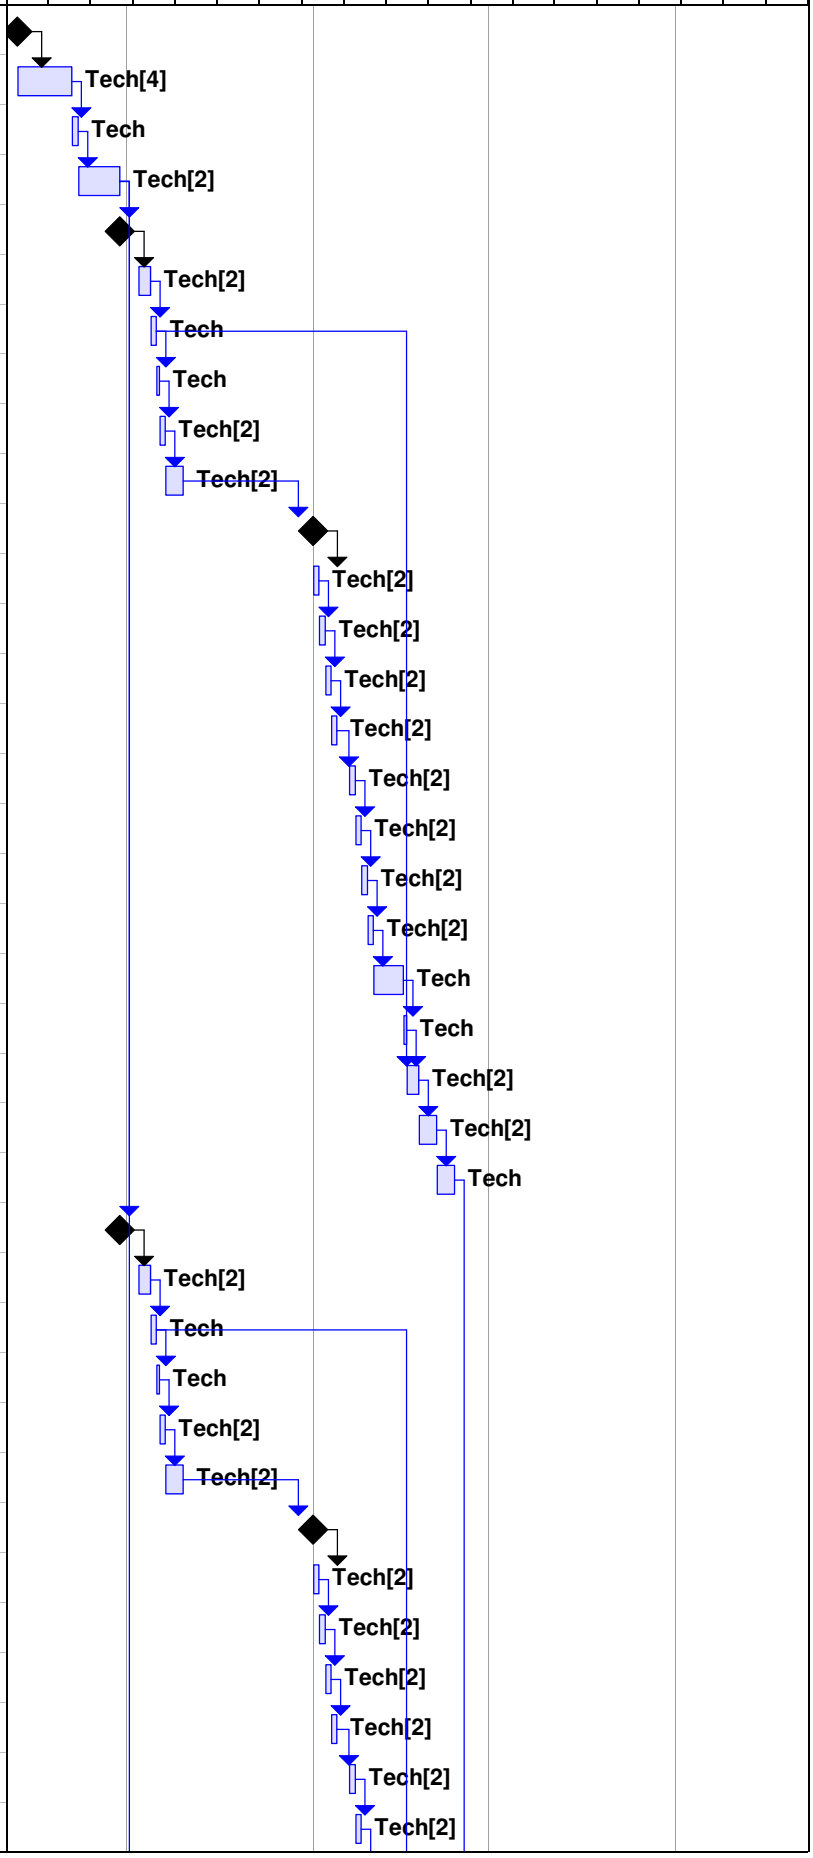

H1 FORWARD TRACKER
SHUTDOWN SCHEDULE

Fri 11/12/98
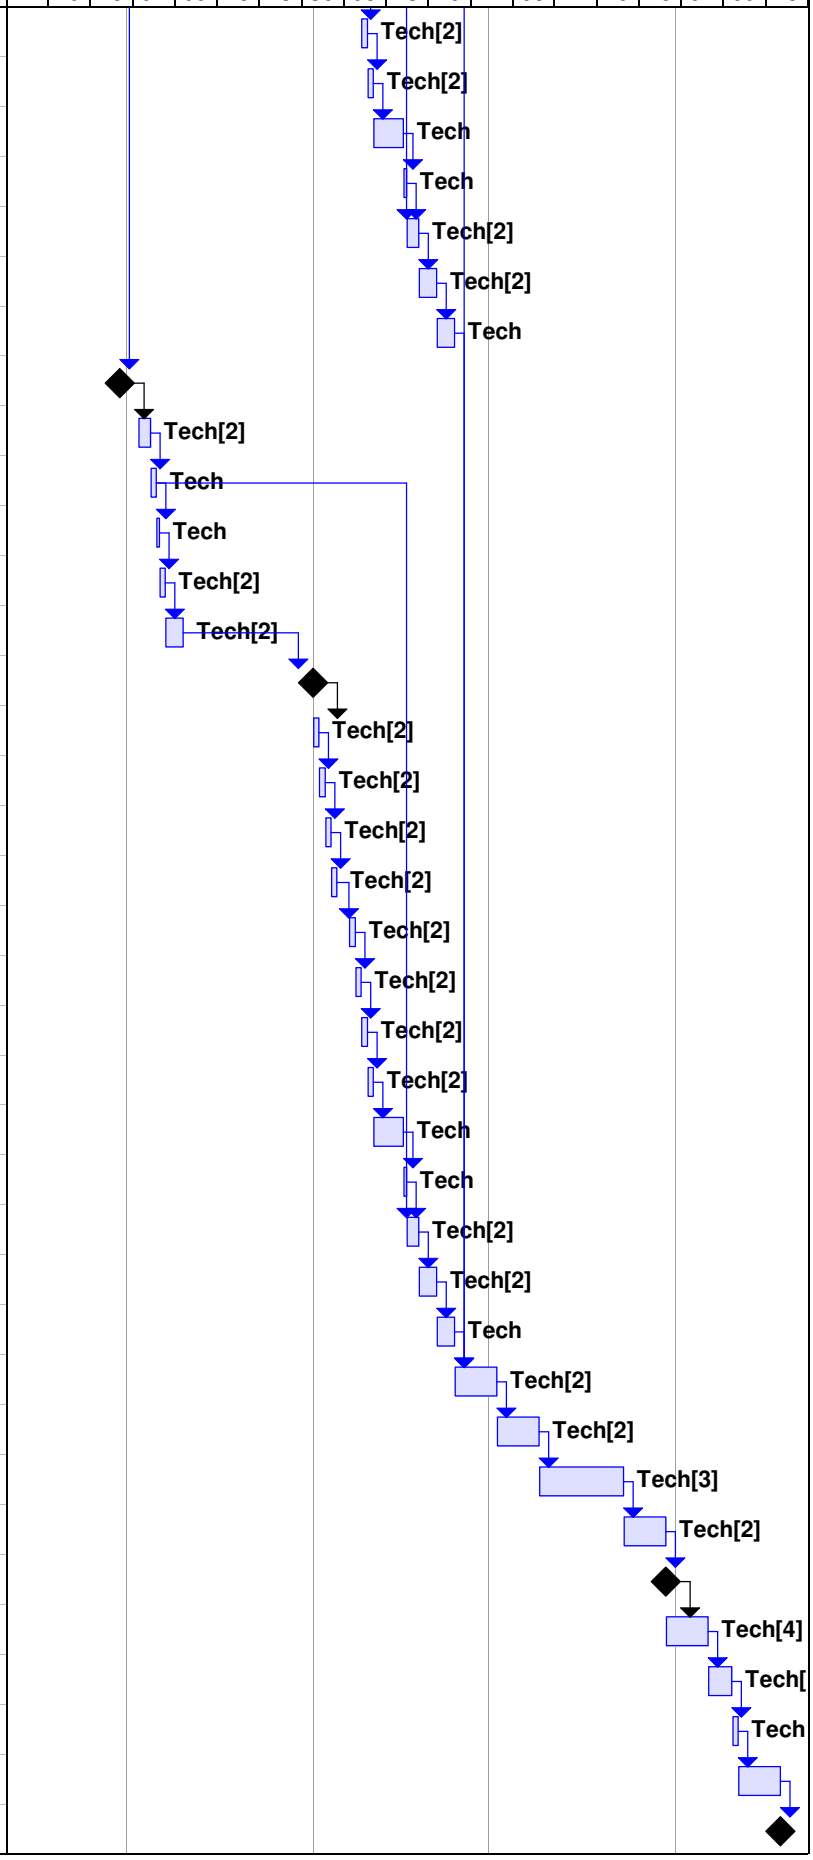
ID	Task Name	Duration
38	Fit 4 wire planar and level	1d
39	Wire-up, solder, plug & test	1d
40	Box up,gas up,volts on and test	3d
41	Flip supermodule	0.5d
42	Install radial chamber and tank segm	2d
43	Reconnect radial chamber	1d
44	Box up,gas up,volts on and test	3d
45	Supermodule3	1d
46	Remove radial chamber and tank se	2d
47	Repair radial module	1d
48	Flip supermodule	0.5d
49	Remove planars	1d
50	Remove MWPCs	1d
51	Planars available	0w
52	Fit 6 wire planar and level	1d
53	Wire-up, solder, plug & test	1d
54	Fit 4 wire planar and level	1d
55	Wire-up, solder, plug & test	1d
56	Fit 4 wire planar and level	1d
57	Wire-up, solder, plug & test	1d
58	Fit 4 wire planar and level	1d
59	Wire-up, solder, plug & test	1d
60	Box up,gas up,volts on and test	3d
61	Flip supermodule	0.5d
62	Install radial chamber and tank segm	2d
63	Reconnect radial chamber	1d
64	Box up,gas up,volts on and test	3d
65	Re-assemble supermodules	5d
66	Check f/thros,gas up and leak chase	5d
67	Reconnect external cables	10d
68	Pulse,preamp and volt tests in air	5d
69	FTD ready to install in H1	0w
70	Install FTD in H1,recable over CT	5d
71	Retest all preamps	2d
72	Push into cryostat	1d
73	Connect cables to CDA panel and te	5d
74	Installation complete	1d
