PLANAR CONSTRUCTION

Fri 11/12/98

ID	Task Name	Duration
1	Start of planar chamber construction	0d
2	Planar chamber No. 1	0d
3	Glue PCB's to Nomex disc (x2) & allow resin to c	5d
4	Dry fit cathode side walls into RH Nomex disc	2d
5	Flip and back fill slots with resin	3d
6	Offer LH disc onto side walls and snap of tongue	2d
7	Flip and back fill slots with resin	3d
8	Transfer assmbly onto wiring table and setup	2d
9	Wiring of chamber no. 1	0d
10	Wire single cell and test (x28)	28d
11	Contingency for cells failures	5d
12	Testing No. 1	0d
13	Volts test in air & check for shorts	2d
14	Planar in gas tank, purge & current checks	3d
15	Remove from gas tank & fit PCB end walls	4d
16	Re-check in gas tank	3d
17	Remove from gas tank & fit RF screen	2d
18	Planar chamber No. 2	0d
19	Glue PCB's to Nomex disc (x2) & allow resin to c	5d
20	Dry fit cathode side walls into RH Nomex disc	2d
21	Flip and back fill slots with resin	3d
22	Offer LH disc onto side walls and snap of tongue	2d
23	Flip and back fill slots with resin	3d
24	Transfer assmbly onto wiring table and setup	2d
25	Wiring of chamber no. 2	0d

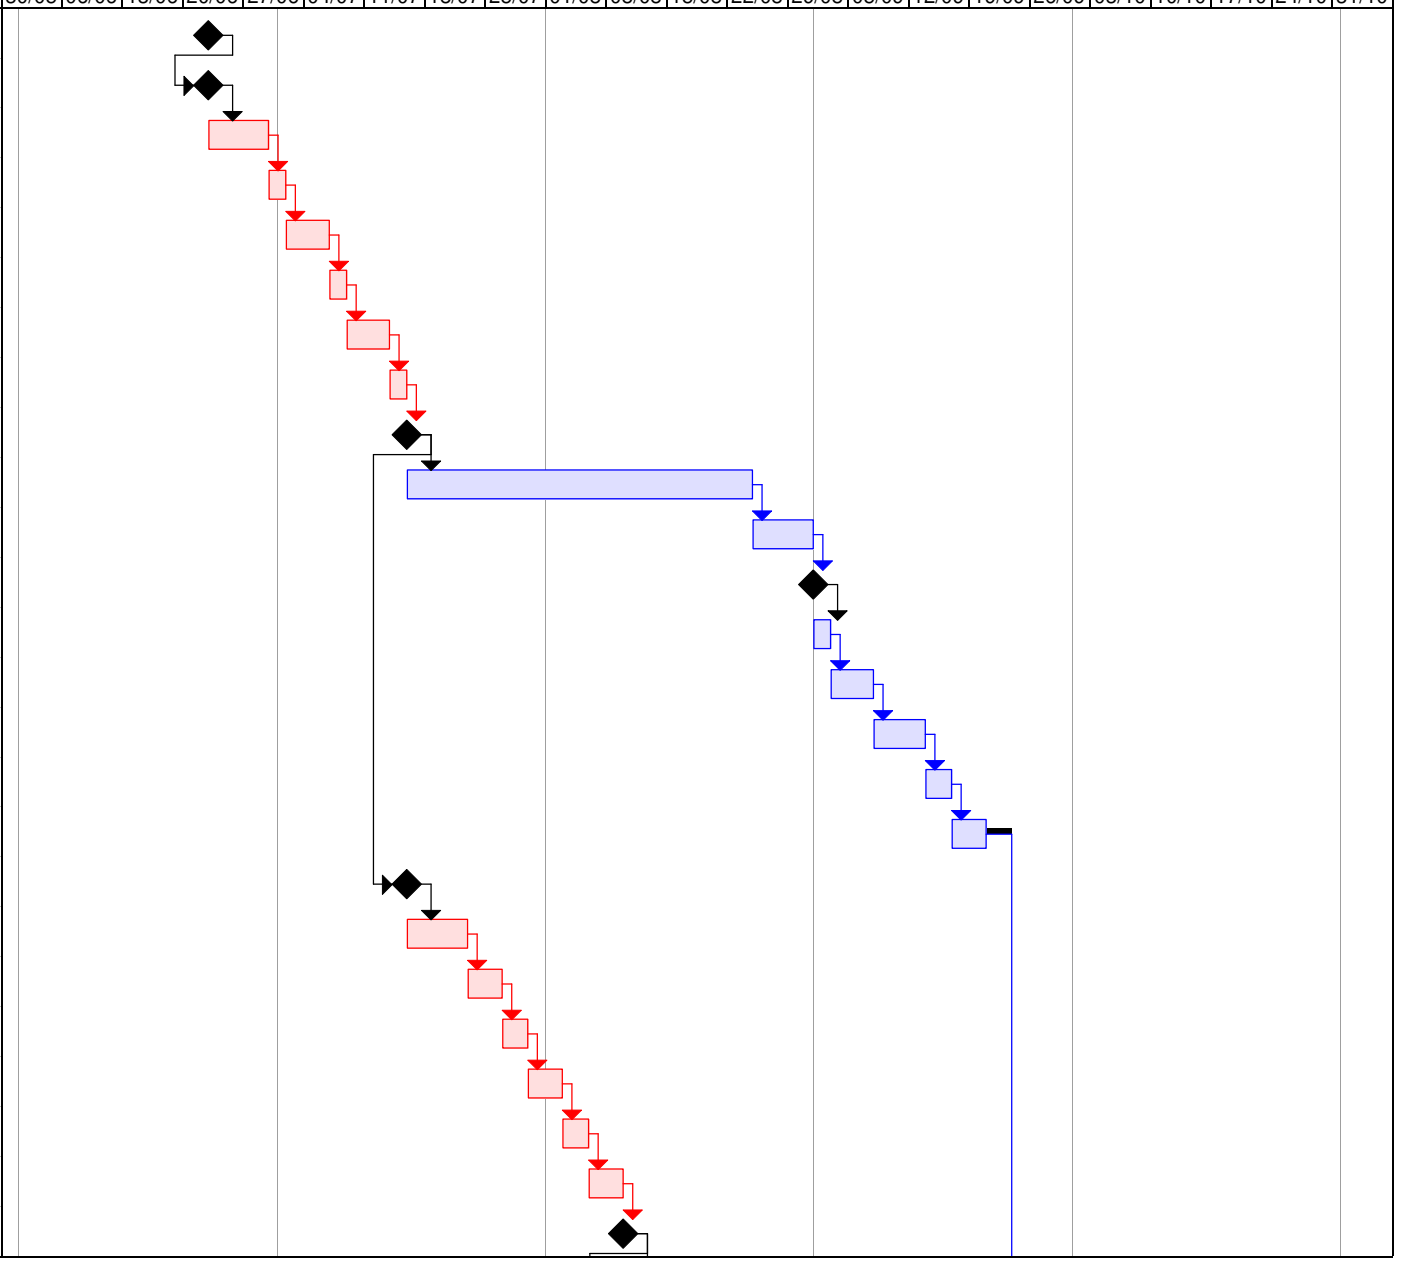

PLANAR CONSTRUCTION

Fri 11/12/98
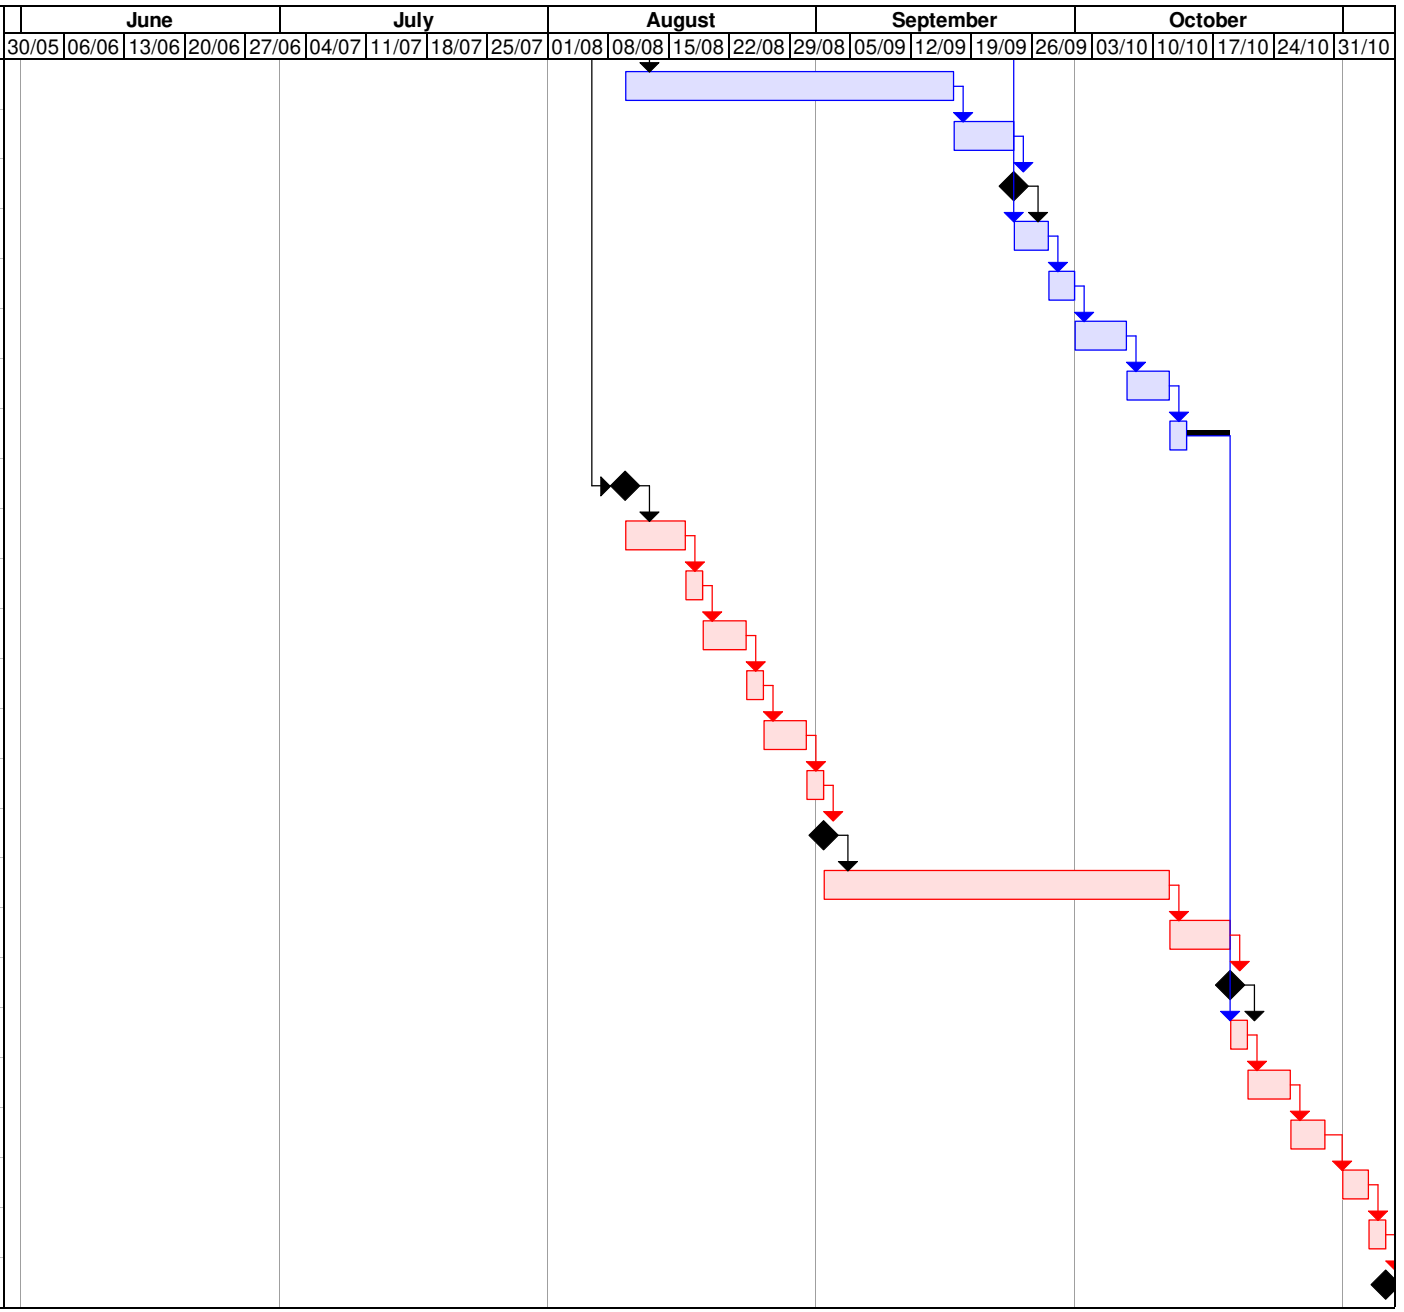
ID	Task Name	Duration
26	Wire single cell and test (x28)	28d
27	Contingency for cells failures	5d
28	Testing No. 2	0d
29	Volts test in air & check for shorts	2d
30	Planar in gas tank, purge & current checks	3d
31	Remove from gas tank & fit PCB end walls	4d
32	Re-check in gas tank	3d
33	Remove from gas tank & fit RF screen	2d
34	Planar chamber No. 3	0d
35	Glue PCB's to Nomex disc (x2) & allow resin to c	5d
36	Dry fit cathode side walls into RH Nomex disc	2d
37	Flip and back fill slots with resin	3d
38	Offer LH disc onto side walls and snap of tongue	2d
39	Flip and back fill slots with resin	3d
40	Transfer assmbly onto wiring table and setup	2d
41	Wiring of chamber no. 3	0d
42	Wire single cell and test (x28)	28d
43	Contingency for cells failures	5d
44	Testing No. 3	0d
45	Volts test in air & check for shorts	2d
46	Planar in gas tank, purge & current checks	3d
47	Remove from gas tank & fit PCB end walls	4d
48	Re-check in gas tank	3d
49	Remove from gas tank & fit RF screen	2d
50	Planar construction conpleted	0d
