PLANAR CONSTRUCTION

Thu 11/05/00
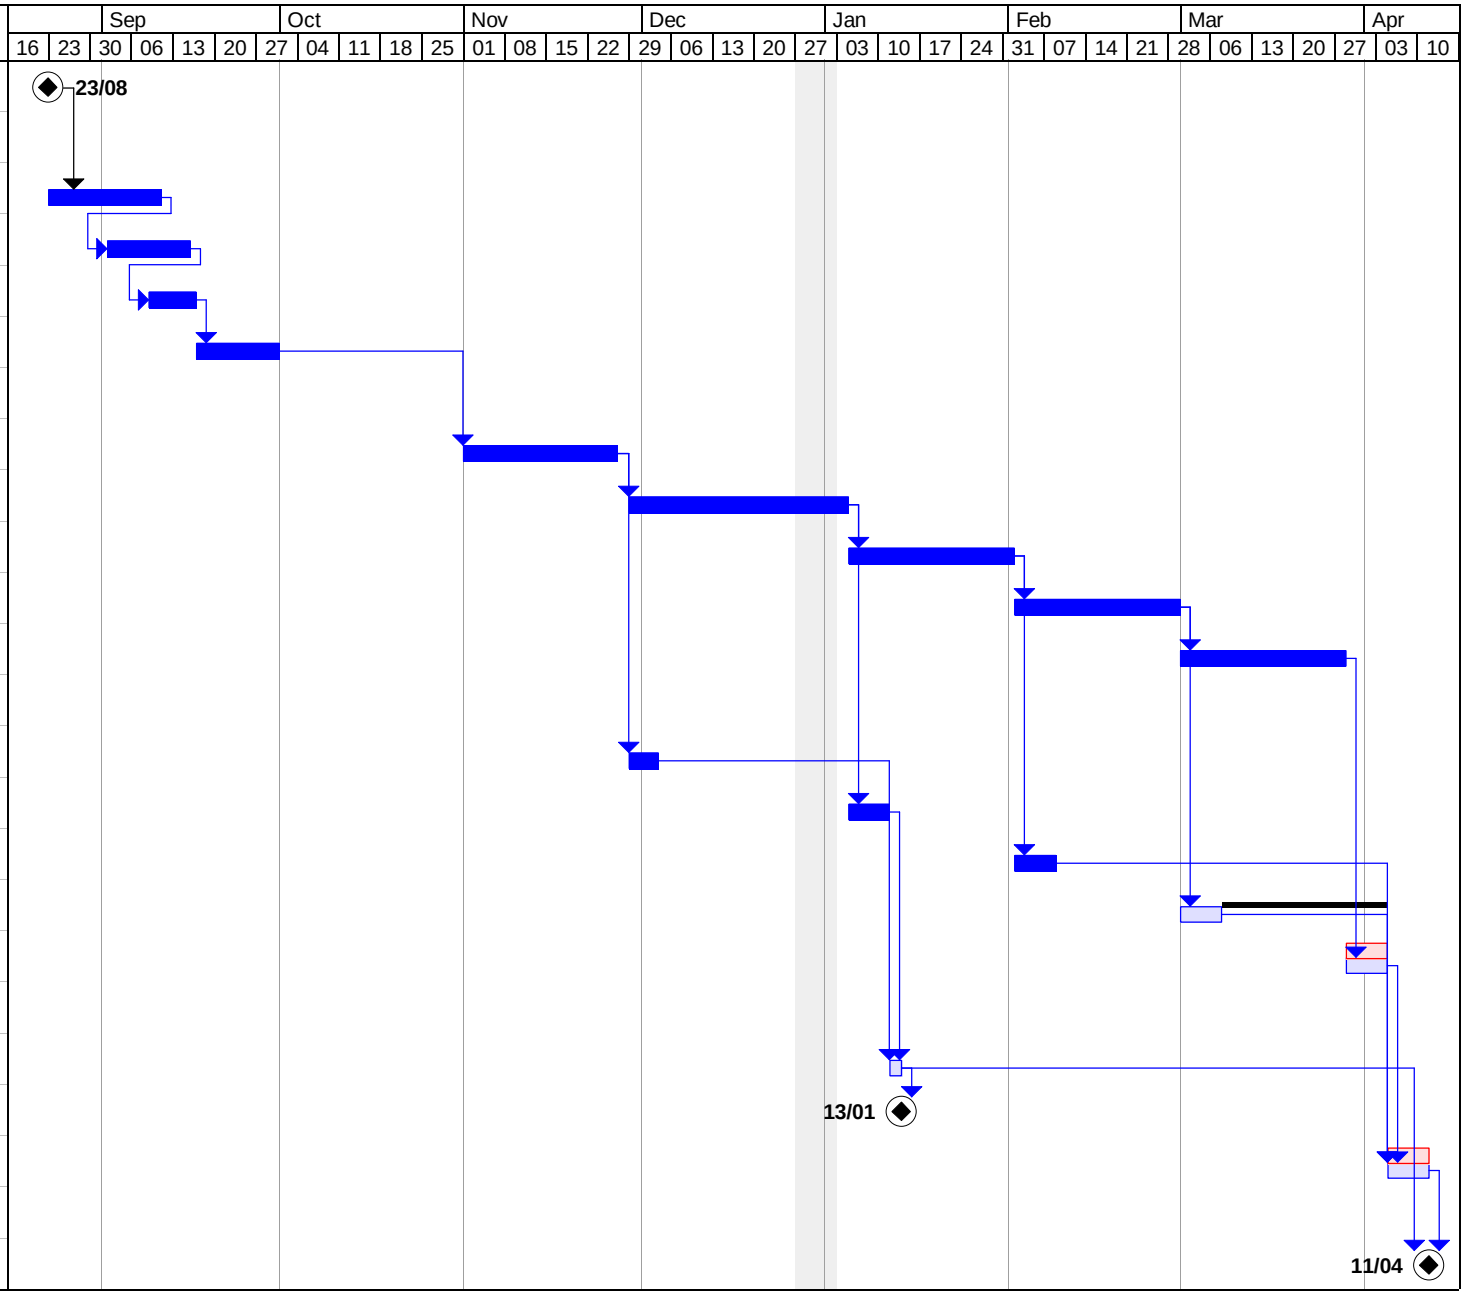
ID	Task Name	Duration
1	Start planar construction	0 days
2		
3	Clean and HV test PCB's	15 days
4	Bond PCB's to Nomex panels	10 days
5	HV test bonded PCB's	6 days
6	Construct 5 chambers	10 days
7		
8	Wire and tension test planar no. 1	20 days
9	Wire and tension test planar no. 2	20 days
10	Wire and tension test planar no. 3	20 days
11	Wire and tension test planar no. 4	20 days
12	Wire and tension test planar no. 5	20 days
13		
14	Planar 1 electrical	5 days
15	Planar 2 electrical	5 days
16	Planar 3 electrical	5 days
17	Planar 4 electrical	5 days
18	Planar 5 electrical	5 days
19		
20	Fit manifold, foil etc. to planar 1 & 2	2 days
21	Start of planar testing	0 wks
22	Fit manifold, foil etc. to planars 3,4,5	5 days
23		
24	Planar construction completed	0 days
