H1 FORWARD TRACKER UPGRADE SCHEDULE

Fri 11/12/98

ID	Task Name
1	Project start
2	Develop specification through feasibility stage
3	Agree project specification and fund project
4	FTD simulation
5	Bank structure
6	Kalmen filter
7	Radial segment finding
8	FTD event display
9	Alignment
10	Planar monitoring and calibration
11	Planar QT hit finding and display
12	
13	Detail electrical and electronic design
14	Detail mechanical design
15	Procure electrical and electronic hardware
16	Procure mechanical hardware
17	Prepare infrastructure
18	
19	Pattern recognition
20	Planar segment linking
21	Software tasks completed
22	Mechanical assembly and test - Planar 1
23	Mechanical assembly and test - Planar 2
24	Mechanical assembly and test - Planar 3
25	Construction of planars completed

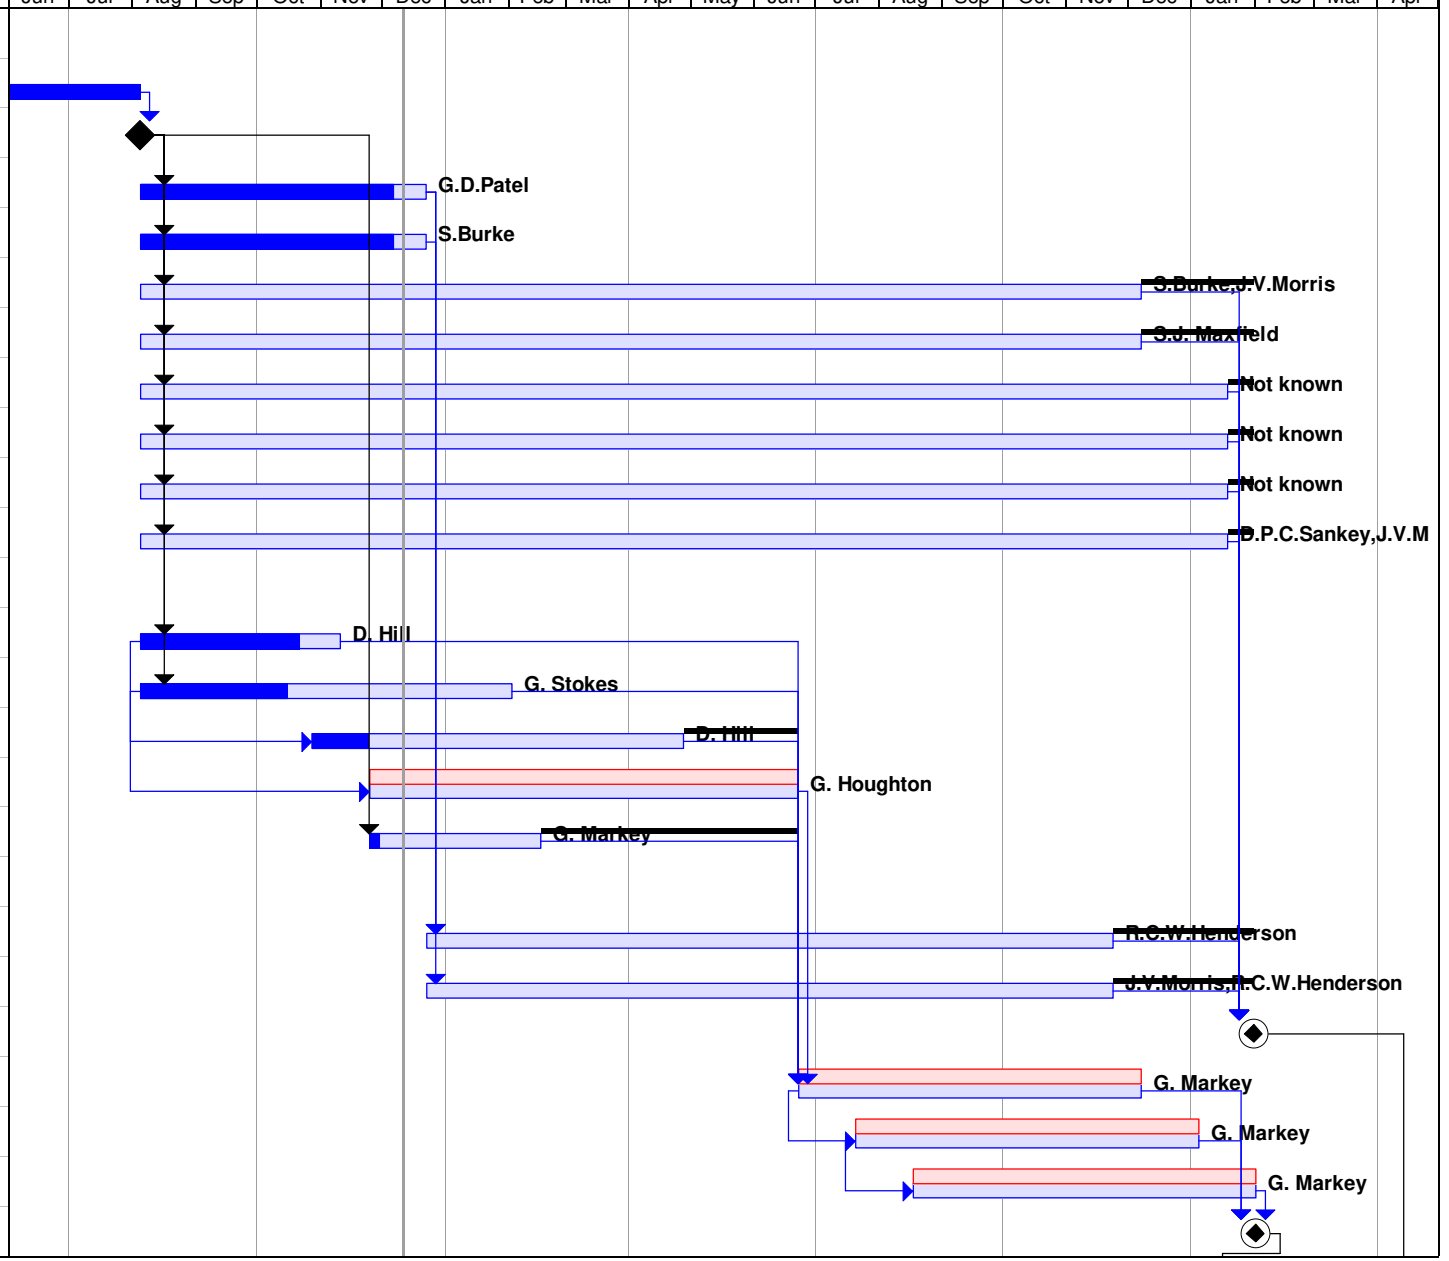

H1 FORWARD TRACKER UPGRADE SCHEDULE

Fri 11/12/98
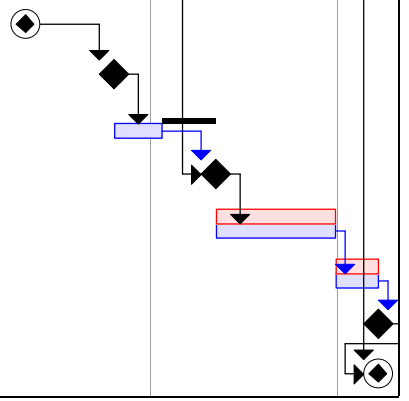
ID	Task Name	8	Qtr 3, 1998			Qtr 4, 1998			Qtr 1, 1999			Qtr 2, 1999			Qtr 3, 1999			Qtr 4, 1999			Qtr 1, 2000			Q
		Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
26																								
27	Start of H1 shutdown																							
28	FTD split from CT																							
29	Move FTD to clean room & split supermodules etc.																							
30	Ready to install planars																							
31	Construct new supermodules and test																							
32	Install FTD in H1																							
33	Installed in H1																							
34	Project complete
